todo-app: end-of-project report


First commit 2026-07-28 – last commit 2026-07-30 · 3 calendar days (2 with commits) · generated 2026-10-19

At a glance

Measure	Value
Commits on `origin/main`	14
Pull requests merged	1 (PR #1, merged 2026-07-30)
Hours	not recorded (no progress ledger)
Cost	not recorded (no progress ledger)
Tasks done / open / dropped	not recorded (no progress ledger; the project has no PLAN.md)
Progress line	not recorded (NEXT.md has no `Progress:` line)
Launch gate	NEXT.md has no launch gate line. It records the site as live at https://dgusti59.github.io/todo-app/ (as recorded in NEXT.md, updated 2026-09-21; not re-checked for this report)

The project is a three-file vanilla HTML, CSS and JavaScript todo app (`index.html` 73 lines, `style.css` 294, `script.js` 302) that keeps its data in `localStorage` and is served from `main` by GitHub Pages. NEXT.md, updated 2026-09-21, calls it a "Finished, deployed vanilla-JS MVP", with two blockers that only the owner can clear.

Progress

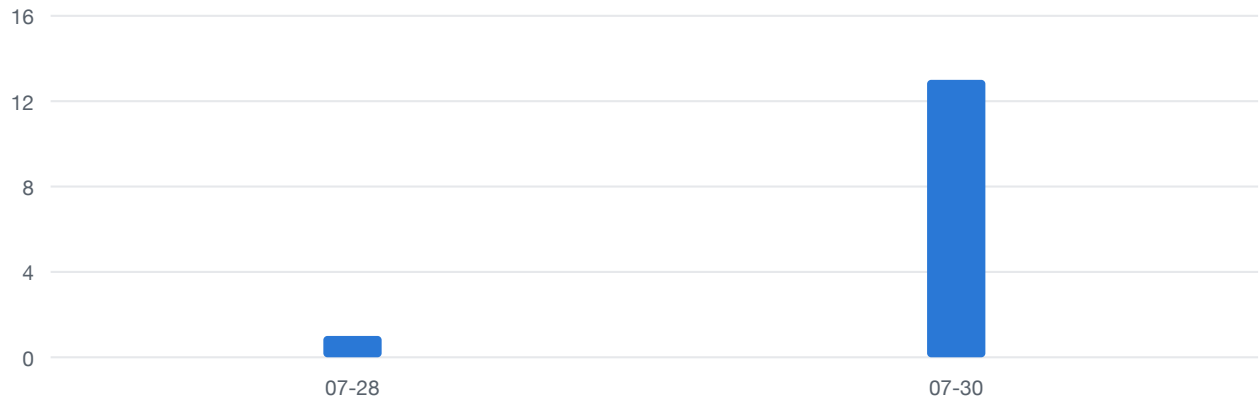

Commits per day on the default branch (days without commits omitted). This project has no progress ledger, so tasks done per day are not recorded.

Date	Done/total	%	Commits	PRs	Sessions	Hours	Reopened
2026-07-28	not recorded	not recorded	1	0	—	—	not recorded
2026-07-30	not recorded	not recorded	13	1	—	—	not recorded

There is no progress ledger, so task counts, sessions, hours and reopen events per day are not recorded. Any 0 or null the generated data shows for reopened means there are no ledger rows, not that zero reopens were seen. The commit and PR figures come from git and `gh`.

Why it took the time it did

The build itself was short. The record shows a stub first commit on 2026-07-28 (`README.md`, 11 bytes) and the whole app on 2026-07-30: `git log --date=iso` dates the 13 commits that day from 14:50:43 to 15:38:11 (+0200), ending in the merge of PR #1. What remains open is about the time after that, not the build.

- **Scope growth:** not recorded (no progress ledger). There was no plan of record at the start or later. NEXT.md: "Plan of record: — (none exists)".
- **Rework:** reopen events, criterion timeouts and refused writes are not recorded (no progress ledger). The git history does show one review cycle. NEXT.md ties two fix commits on 2026-07-30 to the independent review of PR #1 ("Inline-edit save race fixed after independent review — commits `d5e3ea5`, `2cc4a90`"):
  - `d5e3ea5` fixed an inline-edit save race. The Enter and blur paths re-rendered while `editingId` was still set, and a full re-render during a click replaced the DOM node the click was aimed at. The same commit added accessible names, `<label>`s, `aria-pressed`, import error handling and a colour variable.
  - `2cc4a90` covered the case that fix missed: an edit that moves the row outside the active filter or search now falls back to a full render.
  - NEXT.md: "The blur-commit path in `script.js:185-207` is subtle and already cost one review cycle."
- **Waits on the owner:** after the merge on 2026-07-30, nothing was committed. NEXT.md (2026-09-21) records an uncommitted edit dated 2026-08-17 by file time. It added `dev` and `start` scripts to `package.json` and created a `package-lock.json`, which goes against the CLAUDE.md rule that `package.json` "declares no dependencies and has no scripts". Two blockers have waited on the owner since that NEXT.md was written: which of the two is authoritative, and whether any next unit of work exists. NEXT.md says whether the 2026-08-17 edit was deliberate is "unknown — not verified". There is no HISTORY.md, so the reason for the gap between 2026-07-30 and 2026-08-17, and the gap after that, is not recorded.

Direction

There is no PLAN.md. The goal comes from the project's CLAUDE.md: "This is a plain HTML/CSS/JavaScript todo app. These constraints are intentional and must not be relaxed without the user explicitly asking": no framework, no build step, no backend, all data in `localStorage`, deployed to GitHub Pages from `main`. The project memory states the purpose: "the whole point of the project is to exercise core CRUD + persistence features without any tooling overhead."

- 2026-07-30 — CLAUDE.md added (`91eac41`) — to record "the no-framework/no-build/no-backend/localStorage-only rules and the branch-then-PR git workflow this project was actually built under, so future sessions don't drift from them" (commit message).
- 2026-07-30 — the blur-commit edit path changed from a full `render()` to patching only its own row (`d5e3ea5`), then gained a fallback to a full render when the edited row leaves the active filter (`2cc4a90`)

— `d5e3ea5`'s message says it addresses review feedback; NEXT.md ties both commits to the independent review before merge ("Inline-edit save race fixed after independent review — commits `d5e3ea5`, `2cc4a90`").
- 2026-08-17 (file time, from NEXT.md) — `package.json` gained `dev` and `start` scripts, both `python3 -m http.server 3004`, and a `package-lock.json` appeared. Neither file was committed. This contradicts the CLAUDE.md stack rule, and the record does not say why it was done.
- 2026-09-21 — the project was brought under NEXT.md status tracking: NEXT.md written ("Updated: 2026-09-21") and a "Session status" section added to CLAUDE.md (file time 2026-09-21 21:42). Both changes are uncommitted. `git status` on 2026-10-19 shows `M CLAUDE.md`, `M package.json`, `?? NEXT.md` and `?? package-lock.json`.

What shipped

There are no initiatives (no PLAN.md). By NEXT.md workstream:

- **MVP feature set** — add, toggle, delete, inline edit, filters and search with a counter, persisted light and dark theme, JSON import and export, keyboard navigation, responsive layout. Evidence: PR #1 "Add plain HTML/CSS/JS todo app with localStorage persistence", merged 2026-07-30 as `7941280`.
- **Deploy** — GitHub Pages, legacy build from `main /`. Evidence: as recorded in NEXT.md, updated 2026-09-21, the live URL returned 200 and the deployed commit `7941280` matched `HEAD`, from `gh api repos/dgusti59/todo-app/pages`. Not re-checked for this report.
- **Project rules** — CLAUDE.md with the stack constraints and the git workflow. Evidence: `91eac41`, 2026-07-30.

Still open

From NEXT.md (2026-09-21), plus the current `git status`:

- **Blocker 1: uncommitted `package.json` scripts and `package-lock.json` versus the CLAUDE.md rule** — `awaiting: user`. Diego chooses (a) keep both files and amend the rule, or (b) revert with `git checkout package.json && rm package-lock.json`. Claude carries out the choice.
- **Blocker 2: no defined next unit of work** — `awaiting: user`. Diego names the next unit, or declares the project done.
- **README.md is an 11-byte stub** (Roadmap unit 4, "not started") — who acts is not recorded in NEXT.md.
- **Uncommitted status tracking** — the CLAUDE.md "Session status" section and the untracked NEXT.md are not on `main`. NEXT.md does not list this as a blocker. It needs a branch and a PR under the project's git workflow, once Diego decides to keep them.

Sources

- `node ~/.claude/skills/end/scripts/report-data.mjs <project>` run 2026-10-19: span, commit totals, commits and PRs per day, the PR list (through `gh`), and the errors "no PLAN.md" and "no docs/ledger/progress.tsv".
- `git log --all --date=iso`: commit times on 2026-07-30. `git log` message bodies of `91eac41`, `d5e3ea5` and `2cc4a90`. `git show --stat 7941280`.

- `git status --short` and `git diff` (2026-10-19): the uncommitted `CLAUDE.md` and `package.json` changes, the untracked `NEXT.md` and `package-lock.json`. `stat` file times and `wc -l` line counts.
- Project files: `CLAUDE.md`, `NEXT.md` (Updated 2026-09-21), `README.md`, `package.json`.
- Project memory file `project_todo-app-stack.md`.
- Not present: `PLAN.md`, `HISTORY.md`, `docs/ledger/progress.tsv`.
